

# Harrison Elem. Weekly Blitz: March 27<sup>th</sup>, 2020



**Harrison Elementary:** Bearing walls in Area B continue to rise. The slab on grade prep at the Gym slab is finishing up to prepare for next weeks pour. The underground MEP in the kitchen continues. Bearing CMU continues in the kitchen and restroom core.



# Crosby Elem. Weekly Blitz: March 27<sup>th</sup>, 2020



**Crosby Elementary:** Bearing walls in Area B continue to rise while the foundation CMU moves to the kitchen. At the end of the week, the slab on grade at the Gym will be poured and the underground plumbing will wrap up.



# Miami Whitewater Weekly Blitz: March 27<sup>th</sup>, 2020



**Miami Whitewater Campus:** The South section of the Area B slab on grade has been prepped and will be poured this week. Foundation CMU and the underground MEP continues in Area A.





# Junior High Weekly Blitz: March 27<sup>th</sup>, 2020



**Harrison Junior High:** The Junior High has kicked off with the start of the concrete footers in Area A. The primary electric and site communication feed continue across the site. Logistics gravel has been placed.



# Elementary School Floor Plans

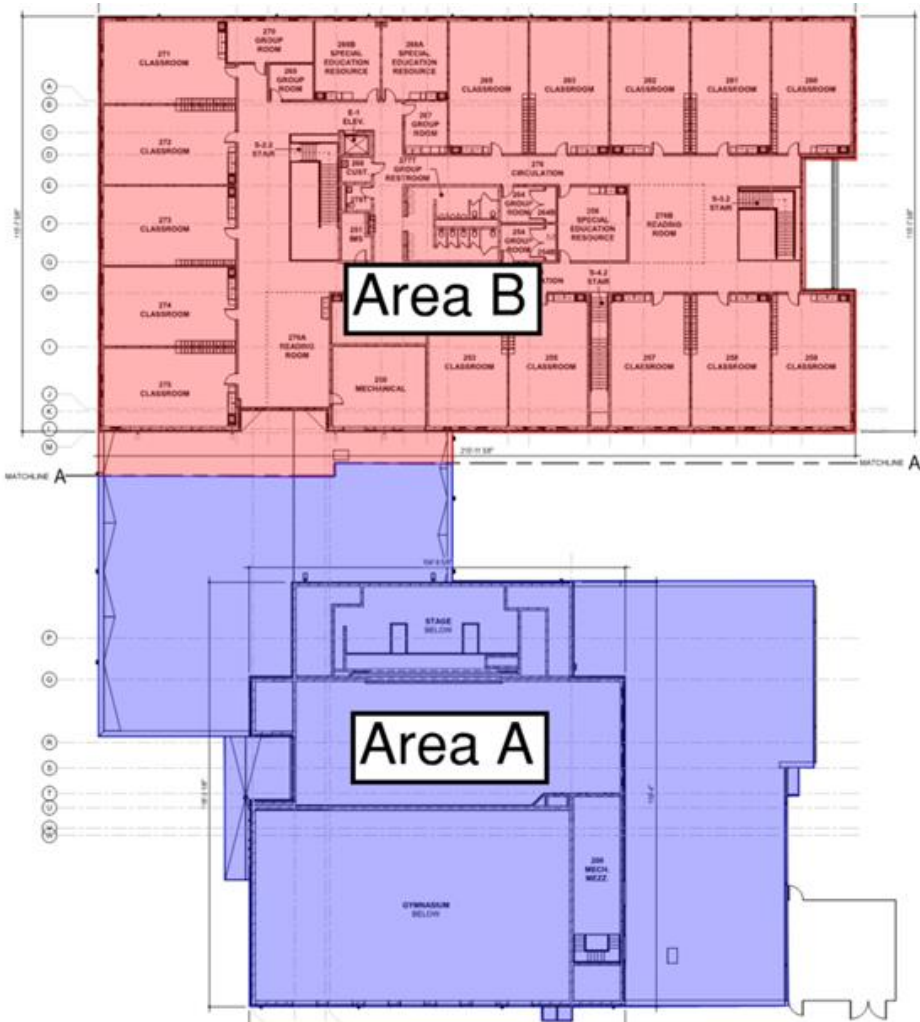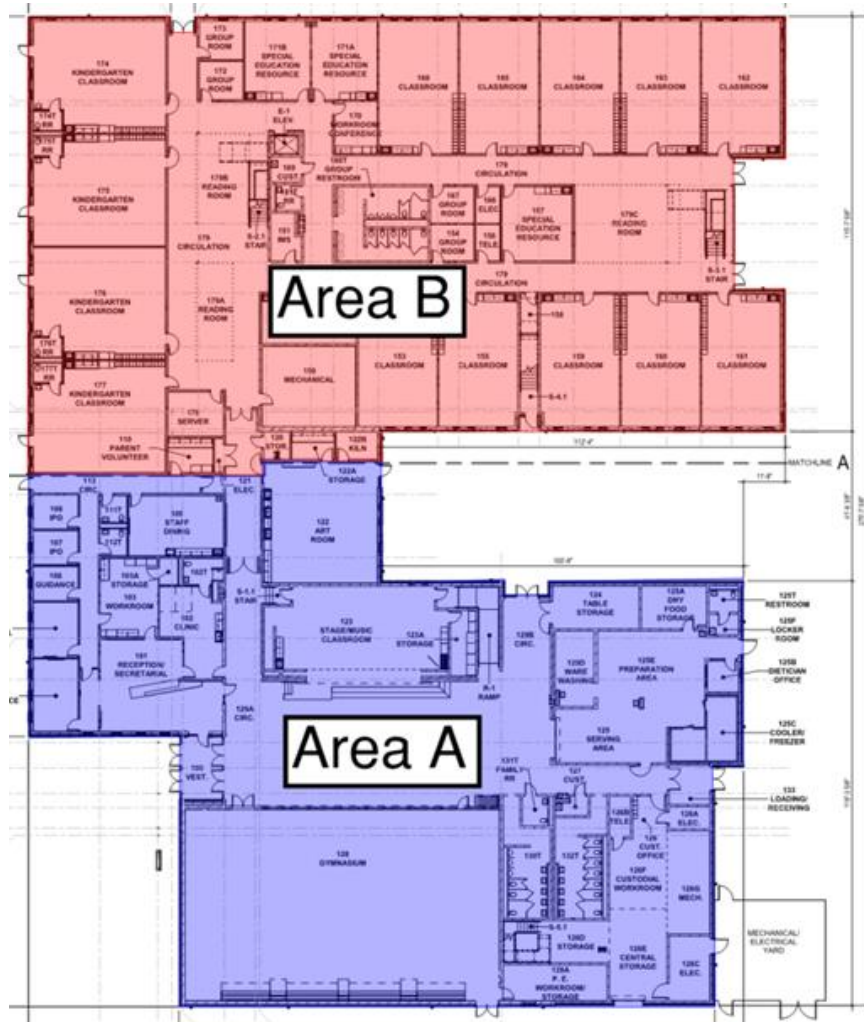

# Junior High School Floor Plans

