

Harrison Elem. Weekly Blitz: April 10th, 2020



Harrison Elementary: The Area B 1st floor North / East bearing wall has been completed and focus has shifted to the Area A stage and admin bearing walls. The kitchen and mechanical slab on grade has been prepped for next week's pour.



Crosby Elem. Weekly Blitz: April 10th, 2020



Crosby Elementary: Bearing walls in Area B continue to rise with the completion of the West wall. The Area B elevator and core walls have been laid out. The kitchen and mechanical room slab on grade was poured this week. Electrical rough-ins on exterior walls and plumbing carriers are being installed.



Miami Whitewater Weekly Blitz: April 10th, 2020



Miami Whitewater Campus:

Foundation block in the kitchen and mechanical room has been completed. The stage, admin, gym, and dining area is being prepped for the slab on grade pour in Area A. Underground plumbing wraps up in Area A ahead of next week's concrete pour.





Junior High Weekly Blitz: April 10th, 2020



Harrison Junior High: The Area B concrete footers continue South towards Area C. The underground plumbing in Area A will finish this week and move to Area B while the primary electrical conduit is being installed in the electrical room. Foundation block is slated to begin next week in Area A



Elementary School Floor Plans

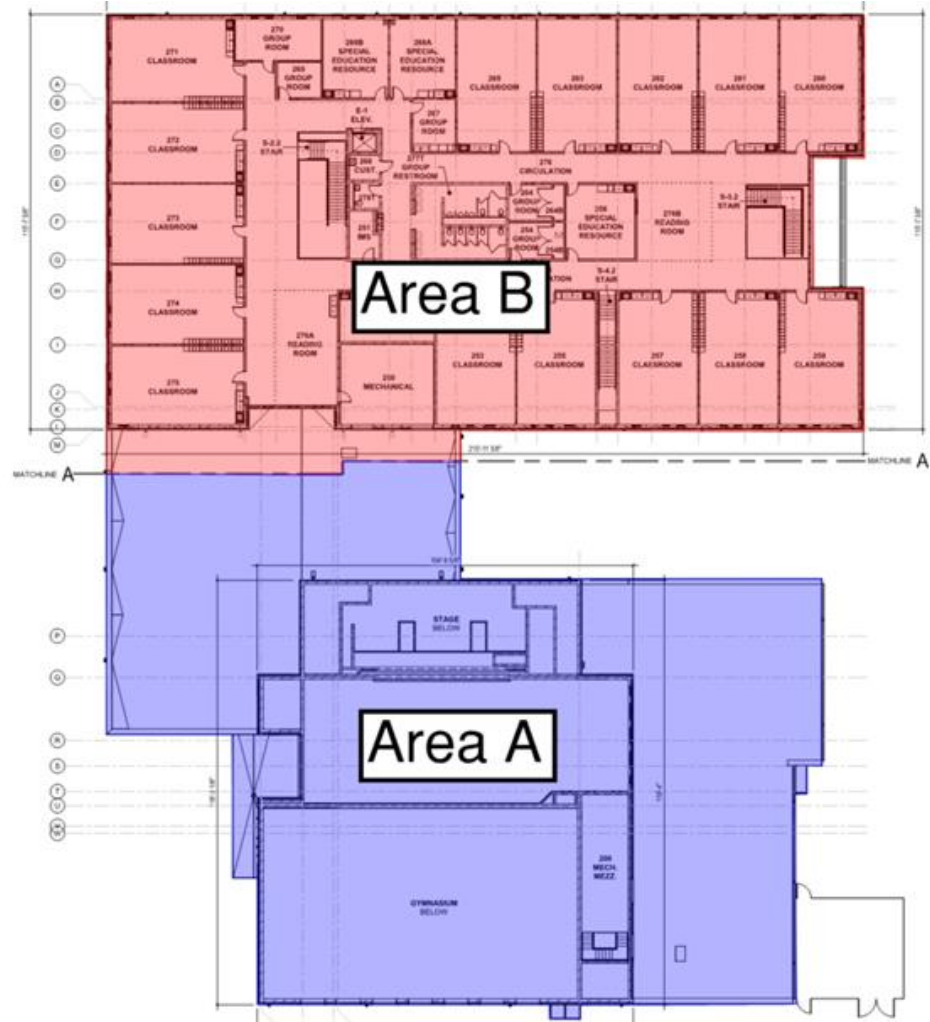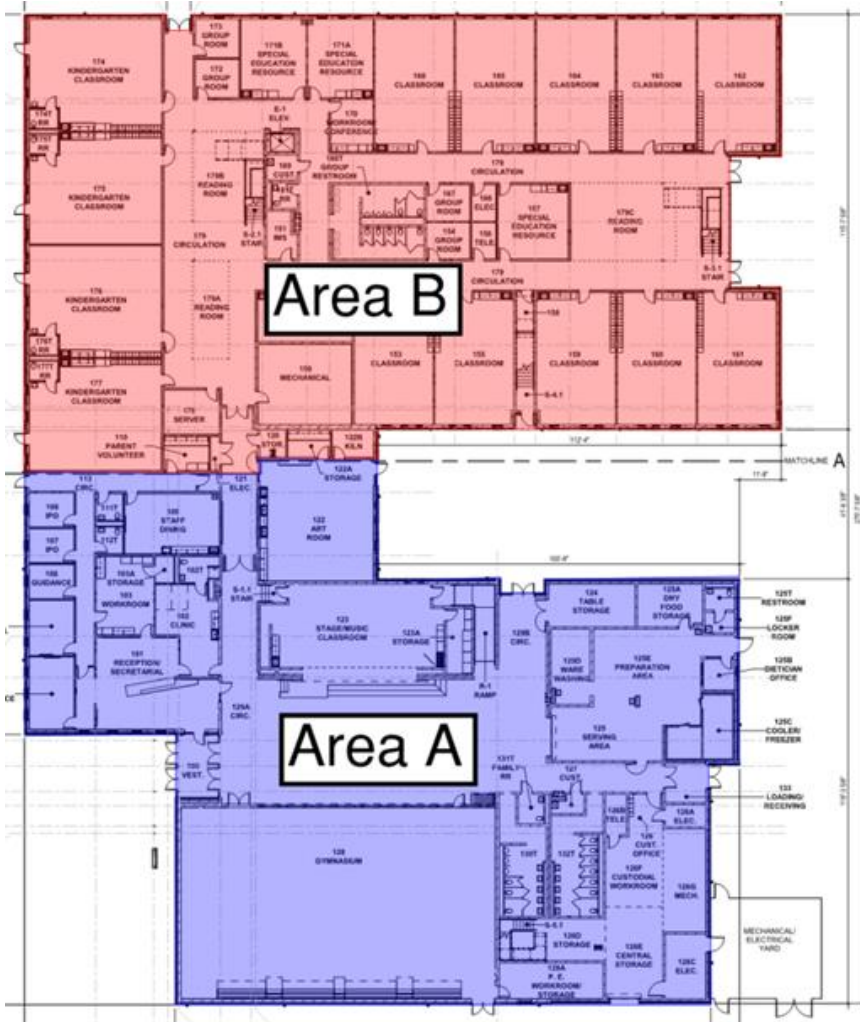

Junior High School Floor Plans

