

Harrison Elem. Weekly Blitz: April 17th, 2020



Harrison Elementary: The Area A stage and admin bearing walls continue to rise. The kitchen and mechanical slab on grade has been poured which completes the 1st floor building slabs. Steel has been delivered and is being set in Area B to kick off Sequence #1.



Crosby Elem. Weekly Blitz: April 17th, 2020



Crosby Elementary: Bearing walls in Area B continue to rise as the masons move to the mechanical and elevator core. The gym bearing walls in Area A have been laid out. Electrical rough-ins on exterior walls and the plumbing carriers continue to be installed across the building.



Miami Whitewater Weekly Blitz: April 17th, 2020



Miami Whitewater Campus: The masons have started the bearing walls in Area B. The slab on grade at the stage, admin, dining, and gym in Area A are being poured this week and the mechanical and kitchen area will be poured next week. Electrical and plumbing rough-ins have begun in Area B.





Junior High Weekly Blitz: April 17th, 2020



Harrison Junior High: Foundation block is being laid in Area A. The concrete footers in Area B are complete and work has begun in Area C. The underground plumbing in Area A has been finished and moved on to Area B while the primary electrical conduit is being installed across the site.



Elementary School Floor Plans

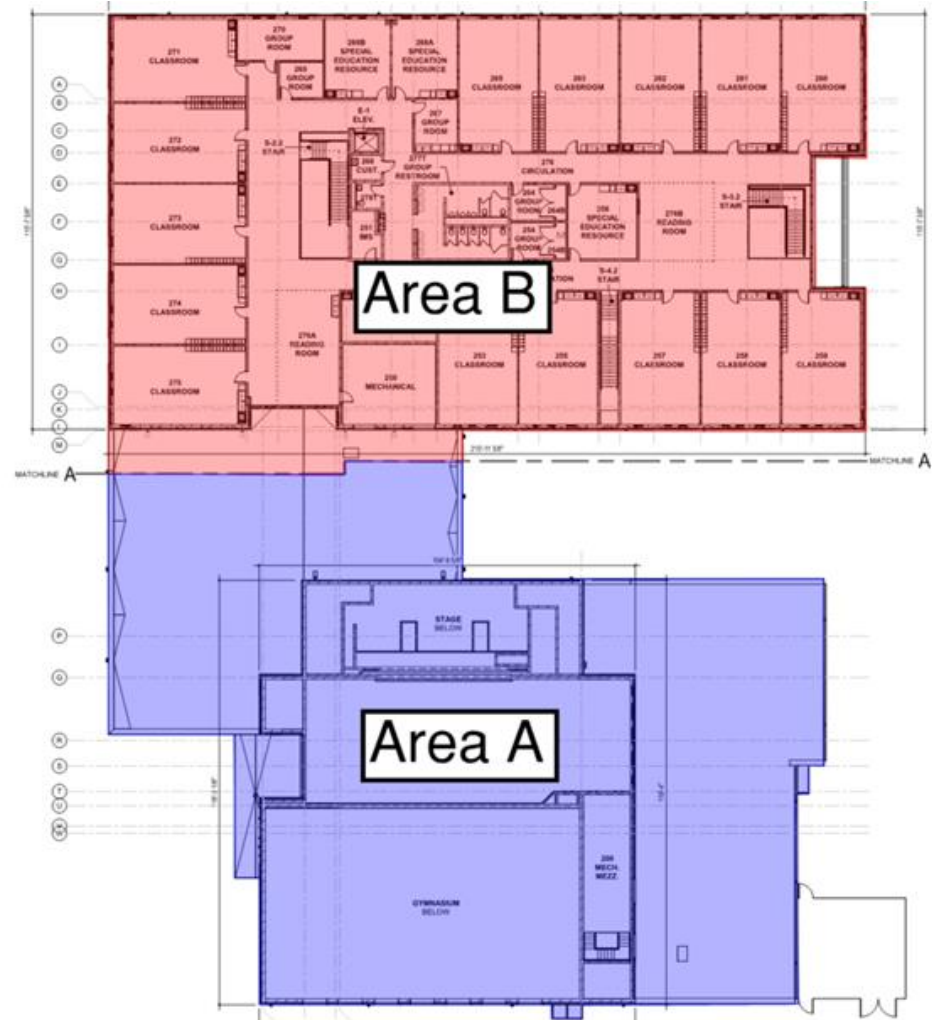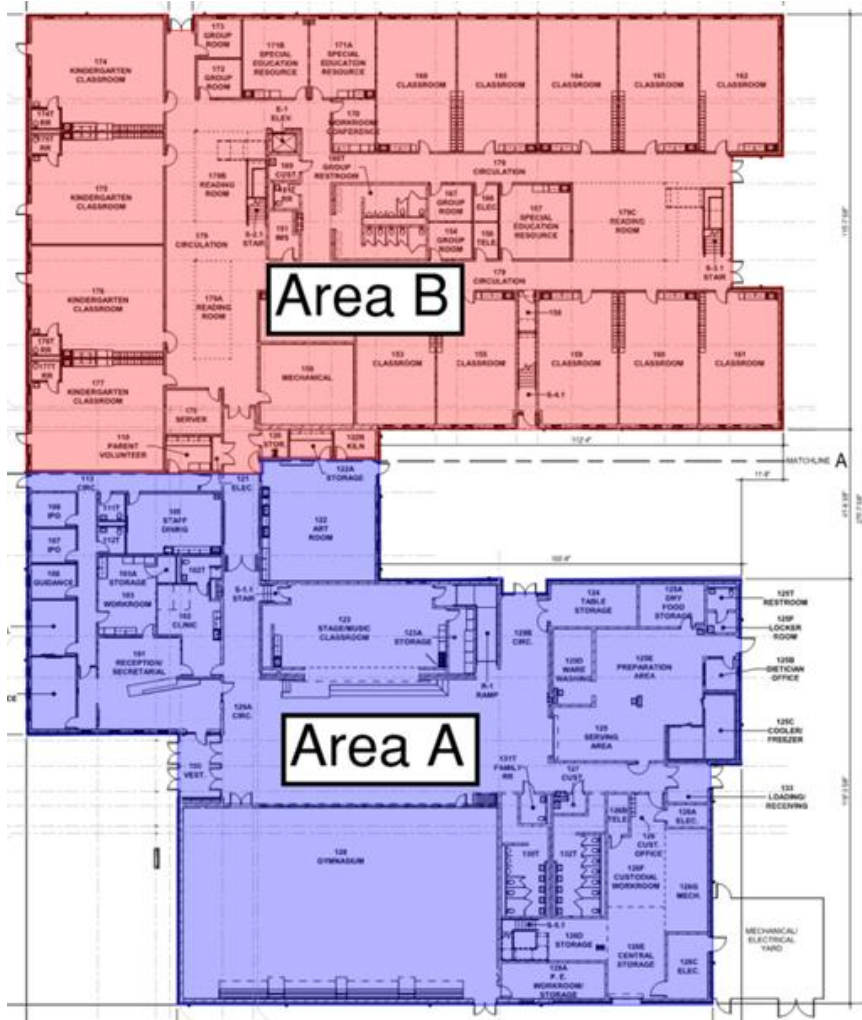

Junior High School Floor Plans

