

# Harrison Elem. Weekly Blitz: July 31<sup>st</sup>, 2020



**Harrison Elementary:** The Area A gym roof is being installed and brick is being laid at the North wall. Drywall is being hung in the 1<sup>st</sup> and 2<sup>nd</sup> floors of the academic wing. In-wall and above ceiling MEP rough-in continues in both Areas. The existing administration building has been demolished.





# Crosby Elem. Weekly Blitz: July 31<sup>st</sup>, 2020



**Crosby Elementary:** In Area A, the roof is being installed at the gym and cafeteria while bearing block and brick is being laid at the main entrance, kitchen, and mechanical room. In Area B, roof steel is being set above the academic wing. In-wall and above ceiling MEP rough-in continues in both Areas.





# Miami Whitewater Weekly Blitz: July 31<sup>st</sup>, 2020



**Miami Whitewater Elementary:** The metal roof decking at the stage and student dining is nearly complete as the gym roof gets installed in Area A. In Area B, the 2<sup>nd</sup> floor block walls are being laid up to the roof level. In-wall and above ceiling MEP rough-in continues throughout Area B.







# Junior High Weekly Blitz: July 31<sup>st</sup>, 2020



**Harrison Junior High:** In the academic wing, the 2<sup>nd</sup> floor bearing walls are rising while the 1<sup>st</sup> floor interior walls are being framed in. The structural steel in the West half of Area B is being set as the East half prepares for an elevated concrete pour. Precast concrete planks have been placed for the 2<sup>nd</sup> floor Area C gym. In-wall and above ceiling MEP rough-in continues.



# Elementary School Floor Plans

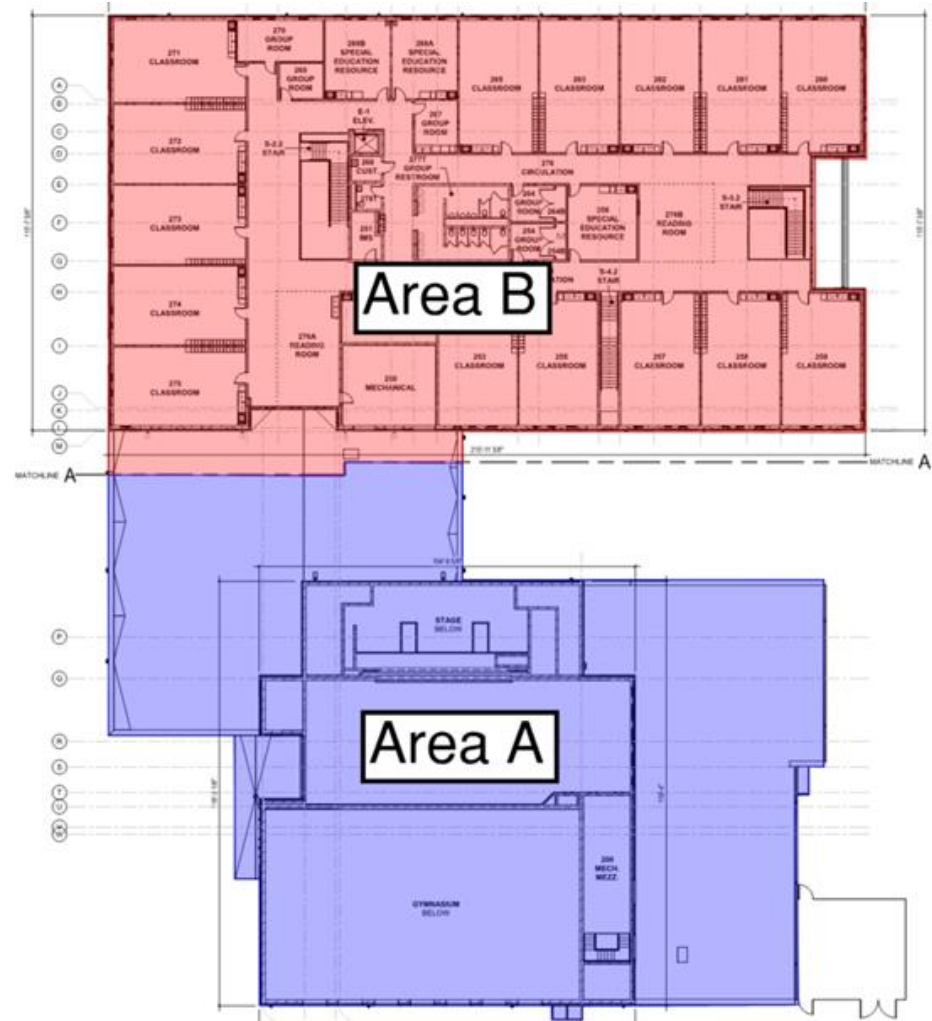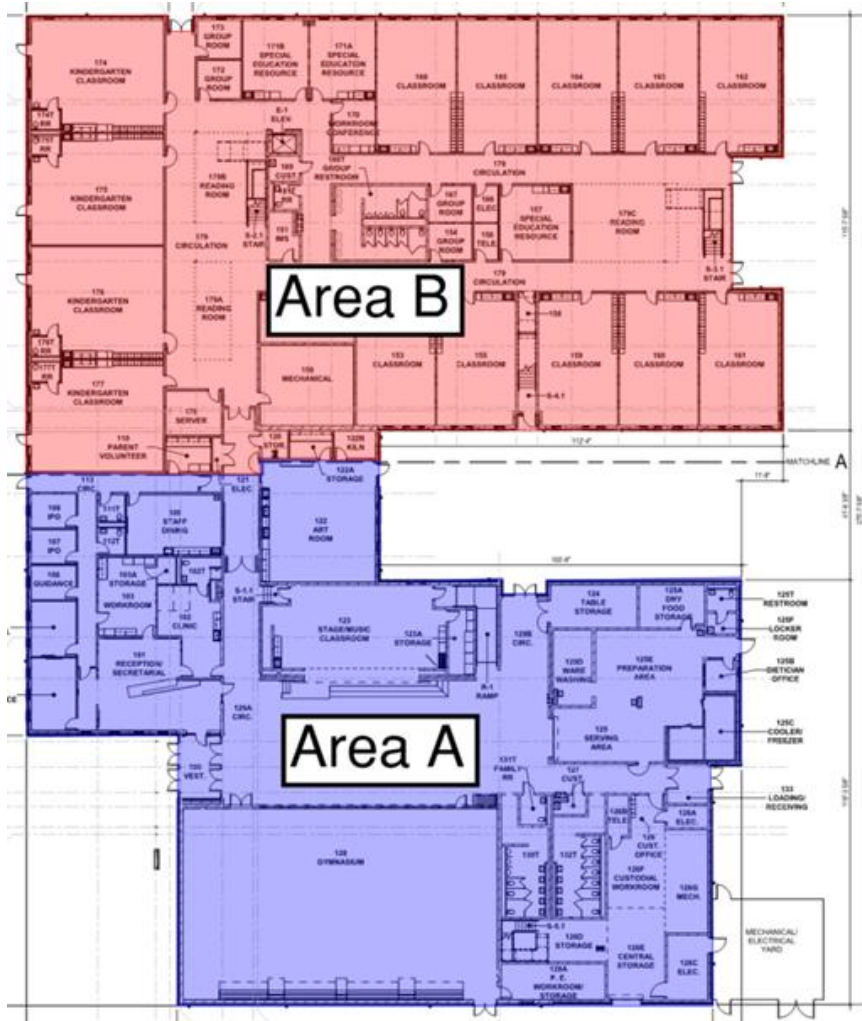



# Junior High School Floor Plans

