



Harrison Elem. Weekly Blitz: August 28th, 2020



Harrison Elementary: In Area A, structural steel is being erected in the art room and administration area while the roof over the kitchen and mechanical room has been installed. In the academic wing, the 1st floor walls are being painted followed by ceiling grid installation while drywall is being hung and finished on the 2nd floor. Brick is being laid in the courtyard between Areas A and B.

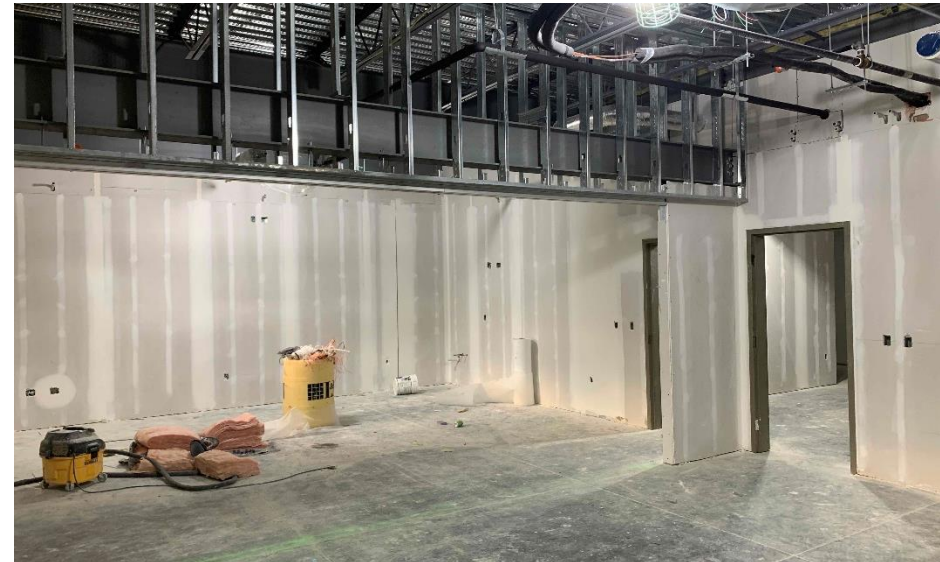

Crosby Elem. Weekly Blitz: August 28th, 2020

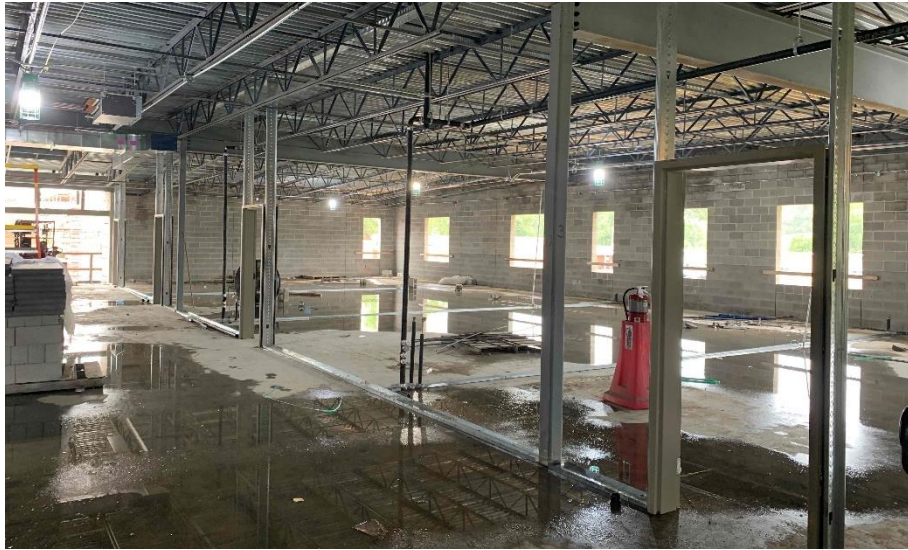

Crosby Elementary: In Area A, the art room bearing block walls will be completed this week while the kitchen is being prepped for structural steel. Roofing installation and the 2nd floor interior wall framing began this week in the academic wing. In-wall and above ceiling MEP rough-in continues in both Areas.



Miami Whitewater Weekly Blitz: August 28th, 2020



Miami Whitewater Elementary: Bearing block walls are being laid in the kitchen, mechanical room, and administration area in Area A. In Area B, structural steel for the roof is being set in the North half of the 2nd floor while the roof is being installed in the South half. The interior walls on the 2nd floor are being laid out. In-wall and above ceiling MEP rough-in continues throughout Area B.




Junior High Weekly Blitz: August 28th, 2020



Harrison Junior High: In the academic wing, structural steel is being erected in the East half of the 2nd floor. The concrete slab for the 3rd floor is scheduled to be poured next week which will complete all building concrete work for the 4 schools. The Area B interior walls are being laid out and framed on the 1st floor and the Area C bearing block walls continue to rise in the kitchen.



Elementary School Floor Plans

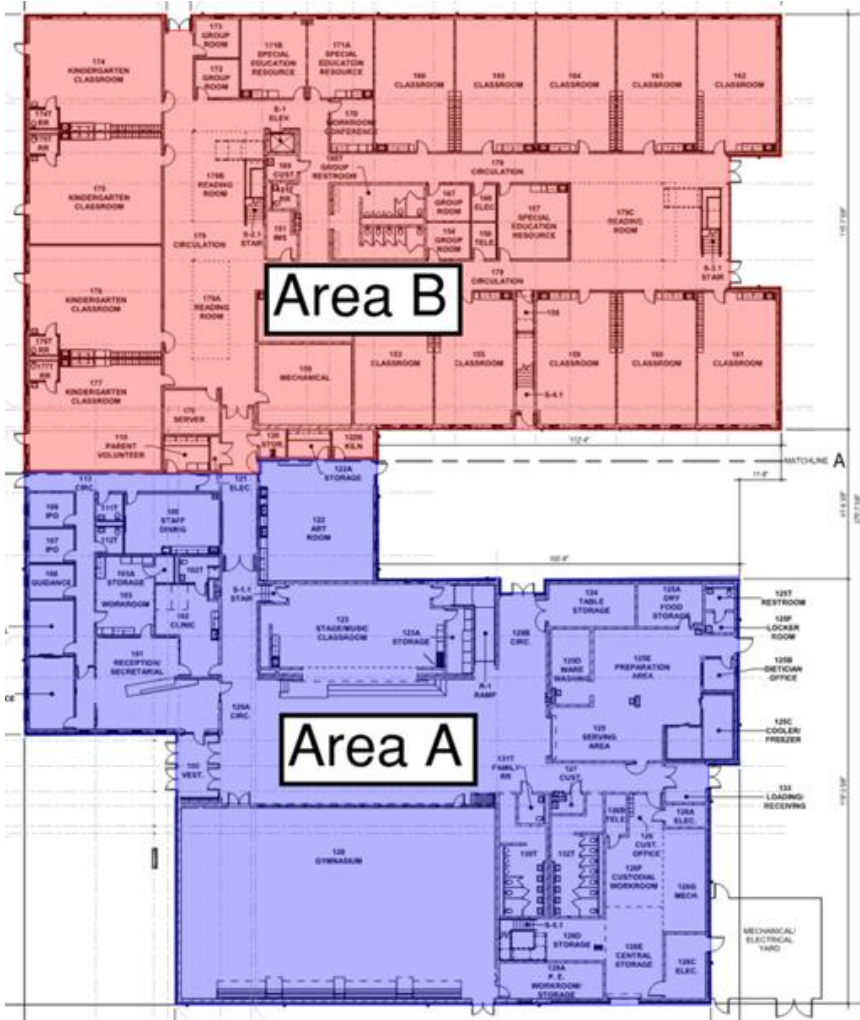

Junior High School Floor Plans

