

Harrison Elem. Weekly Blitz: September 11th, 2020



SKANSKA MEGEN SHP

Harrison Elementary: In Area A, the interior walls are being framed in the art room and administration area while the roof is being installed overhead. In the Area B academic wing, the ceiling grid and lighting has been installed on the 1st floor while drywall is being finished on the 2nd floor. Brick is being laid in the courtyard between Areas A and B. Above ceiling MEP rough-in continues in both Areas.








Crosby Elem. Weekly Blitz: September 11th, 2020



SKANSKA MEGEN SHP

Crosby Elementary: In Area B, drywall is being hung in the 1st floor and block filler is being painted on the CMU walls. On the 2nd floor, interior CMU block walls are being laid around the restrooms and the sprinkler line installation has begun. In-wall and above ceiling MEP rough-in continues in both Areas.

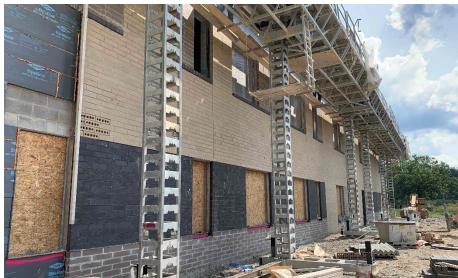



SKANSKA MEGEN SHP



Miami Whitewater Weekly Blitz: September 11th, 2020



Miami Whitewater Elementary: Bearing block walls are being laid in the student dining area and the stage in Area A. Structural steel is being set in the kitchen, mechanical, administration, and art room. In Area B, roof installation continues as the interior walls on the 2nd floor are being laid out and framed. Brick has begun on the East wall of Area B. In-wall and above ceiling MEP rough-in continues throughout Area B.







Junior High Weekly Blitz: September 11th, 2020



SKANSKA MEGEN SHP

Harrison Junior High: In the academic wing, the concrete slab for the 3rd floor has been poured which completes all building concrete work for the four Southwest schools! The interior walls on level 2 are being laid out and framed. Bearing block walls continue to rise in Areas B & C while roof steel is being set on the 2nd floor of Area B. In-wall and above ceiling MEP rough-in continues in both Areas.










2010

JOH MECH MEZZ

Elementary School Floor Plans

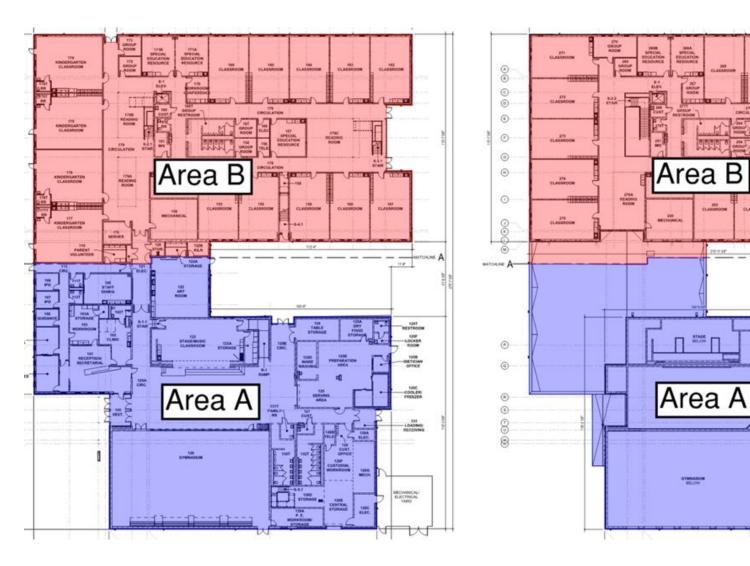





Junior High School Floor Plans

