



Harrison Elem. Weekly Blitz: October 2nd, 2020



Harrison Elementary: The interior block walls are being built in the kitchen in Area A. In the Area B academic wing, the walls are being painted and the bathroom floors are finished. The bathroom accessories and classroom lockers are being installed. On the exterior, brick is being laid on the East wall of Area B and MEP rough-in continues in both Areas.









Crosby Elem. Weekly Blitz: October 2nd, 2020



Crosby Elementary: In Area B, drywall is being hung on the 2nd floor and finished on the 1st floor. In Area A, metal roof decking is being installed above the administration area and interior drywall walls are being framed. Interior block walls are being built in Area A and brick is complete on the North wall of Area B. In-wall and above ceiling MEP rough-in continues in both Areas.









Miami Whitewater Weekly Blitz: October 2nd, 2020



Miami Whitewater Elementary: The roof is being installed above the kitchen, mechanical room, administration, and art room in Area A. The interior walls are being laid out and framed in Area A and drywall is being hung on the 1st floor of Area B. Brick continues on the East wall of Area B. Above ceiling and in-wall MEP rough-in continues in both Areas.









Junior High Weekly Blitz: October 2nd, 2020



Harrison Junior High: Bearing block walls continue to rise in Areas A and C while roof steel is being set on the 2nd floor of Area B. The bus lot sidewalks are being poured and stone is being placed at the access roads in preparation for asphalt. In-wall and above ceiling MEP rough-in continues in all Areas.











Elementary School Floor Plans

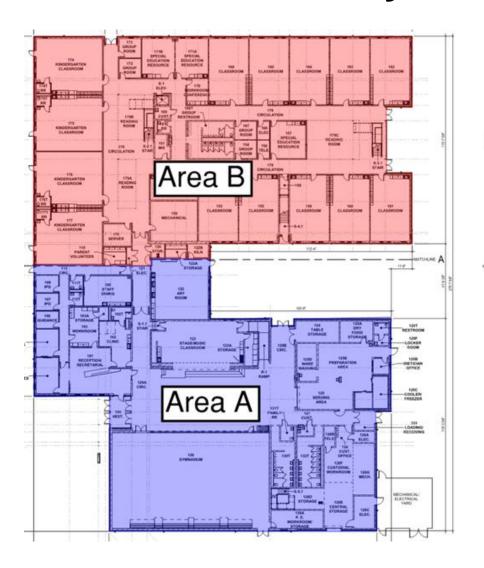


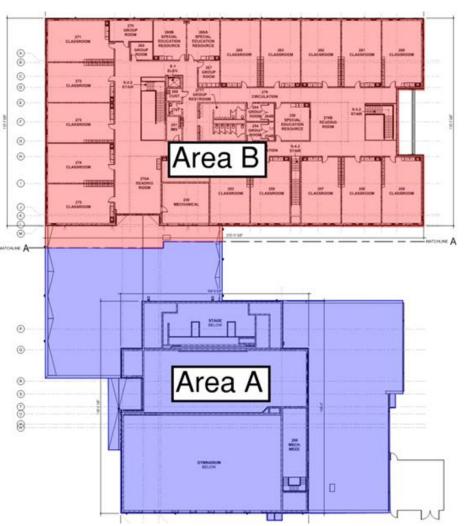






Junior High School Floor Plans

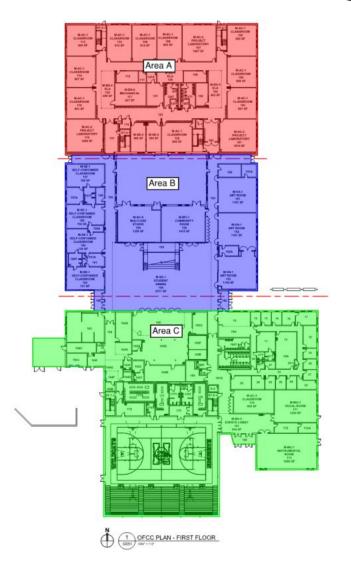

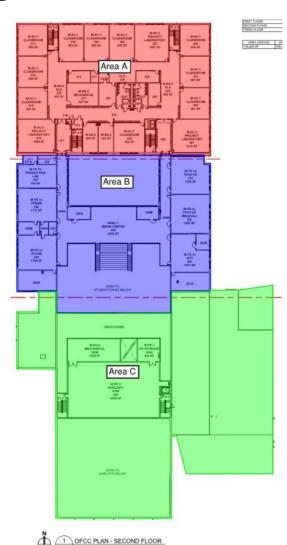



OFCC PLAN - THIRD FLOOR
