

Harrison Elem. Weekly Blitz: October 23rd, 2020




Harrison Elementary: Drywall is being finished in the administration wing while the classroom and gym walls are being painted. Bathroom fixtures and classroom cabinets are being installed on the 1st floor of the Area B academic wing. Window installation continues in Area B and brick has been completed along the North wall. MEP overhead rough-in continues in both Areas.



Crosby Elem. Weekly Blitz: October 23rd, 2020




Crosby Elementary: In Area B, drywall is being finished on the 2nd floor as the 1st floor walls are being painted. Ceiling grid installation has begun. In Area A, drywall is being hung in the administration area and the roof above has been installed. The main entrance and bus entry brick walls have been completed as brick continues along the courtyard. MEP overhead rough-in continues in both Areas.

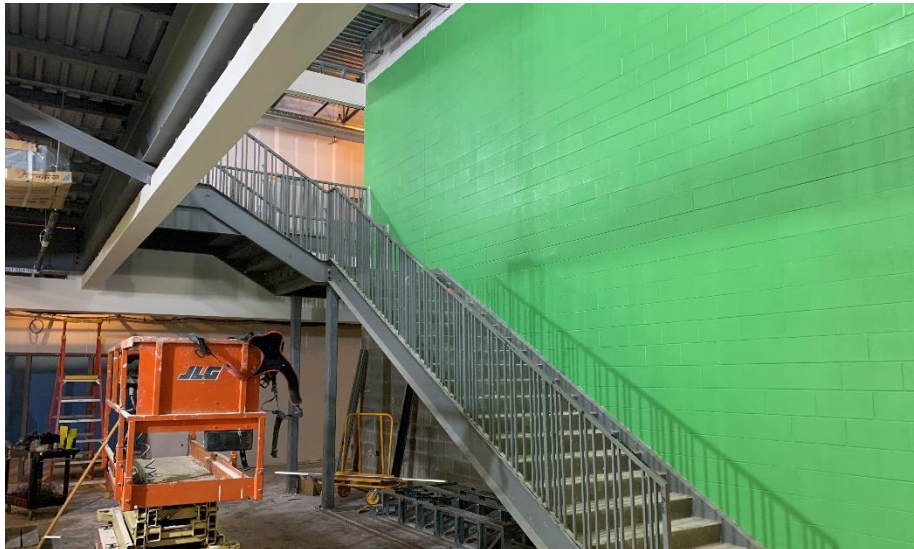

Miami Whitewater Weekly Blitz: October 23rd, 2020



Miami Whitewater Elementary: The 1st floor interior block walls are complete in Area A. In Area B, the 1st floor drywall walls are being finished and primed while the 2nd floor drywall is being hung. Above ceiling and in-wall MEP rough-in continues in both Areas. Concrete sidewalks around the school is ongoing.

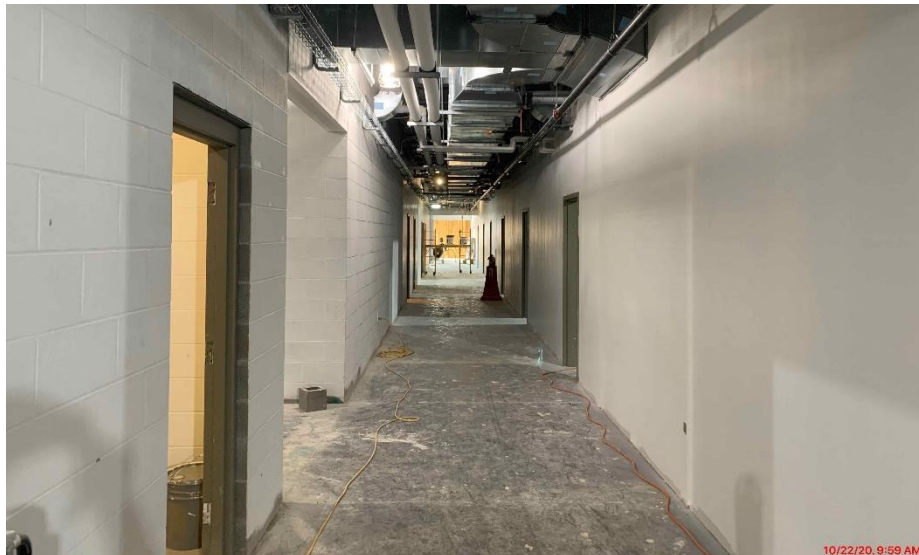


Junior High Weekly Blitz: October 23rd, 2020



Harrison Junior High: Roof steel is being set on the East half of Areas A & B while roof installation has begun on the West half of Area B. Bearing block walls continue to rise in Area C at the main gym and in the administration area. In-wall and above ceiling MEP rough-in continues in all Areas.



Elementary School Floor Plans

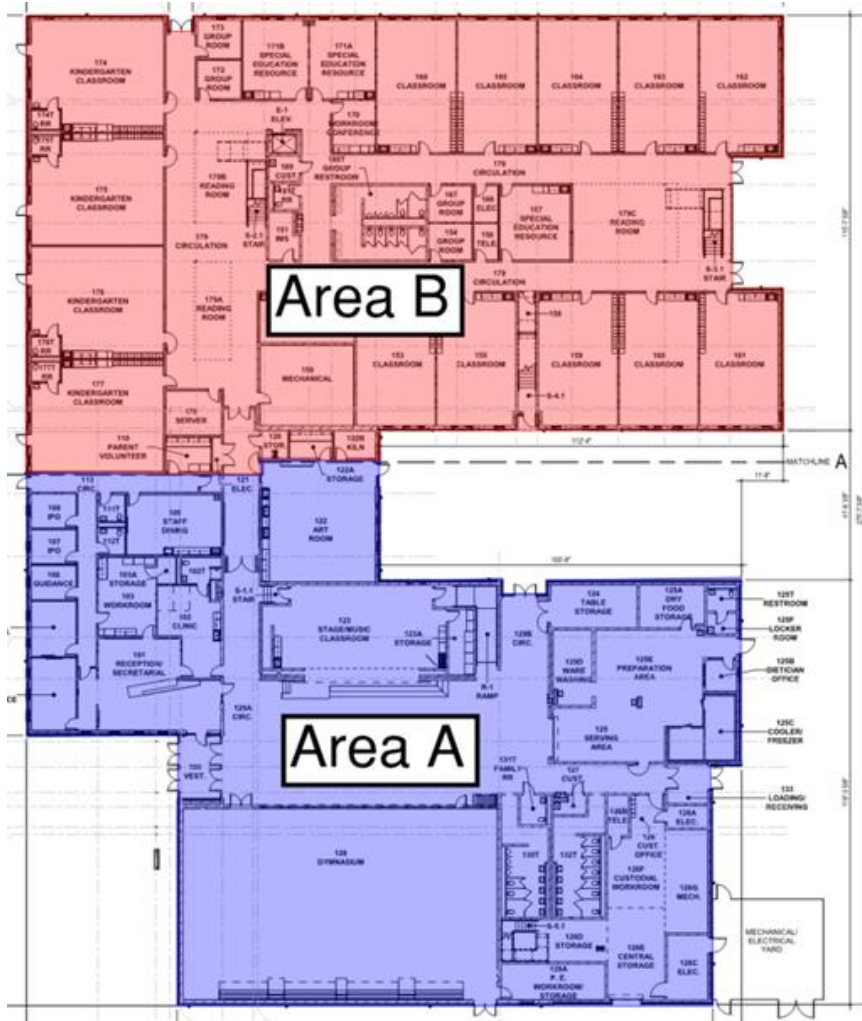

Junior High School Floor Plans

