

Harrison Elem. Weekly Blitz: October 30th, 2020



Harrison Elementary: Drywall is being finished in the administration wing while the classroom and gym walls are being painted. Bathroom fixtures and classroom cabinets are being installed on the 1st floor of the Area B academic wing. Window installation continues in Area B and metal gutters are being installed along the roof. The kitchen cooler in Area A is being installed.



Crosby Elem. Weekly Blitz: October 30th, 2020



Crosby Elementary: In Area B, drywall has been finished on the 2nd floor and the walls are being primed and painted. Ceiling grid installation has been completed on the 1st floor. In Area A, drywall is being hung in the administration area and the kitchen cooler is being installed. Brick work continues along the courtyard. MEP rough-in continues in both Areas.



Miami Whitewater Weekly Blitz: October 30th, 2020



Miami Whitewater Elementary: The interior block walls are nearly complete in Area A and drywall is being hung in the administration wing. In Area B, the 1st floor is being painted with ceiling grid installation following behind and the 2nd floor drywall is being finished. MEP rough-in continues in both Areas.





Junior High Weekly Blitz: October 30th, 2020



Harrison Junior High: Roof steel is complete on the East half of Areas A & B while roof installation continues on the West half of Area B. Bearing block walls continue to rise in Area C at the main gym and in the administration area. In-wall and above ceiling MEP rough-in continues in all Areas.



Elementary School Floor Plans

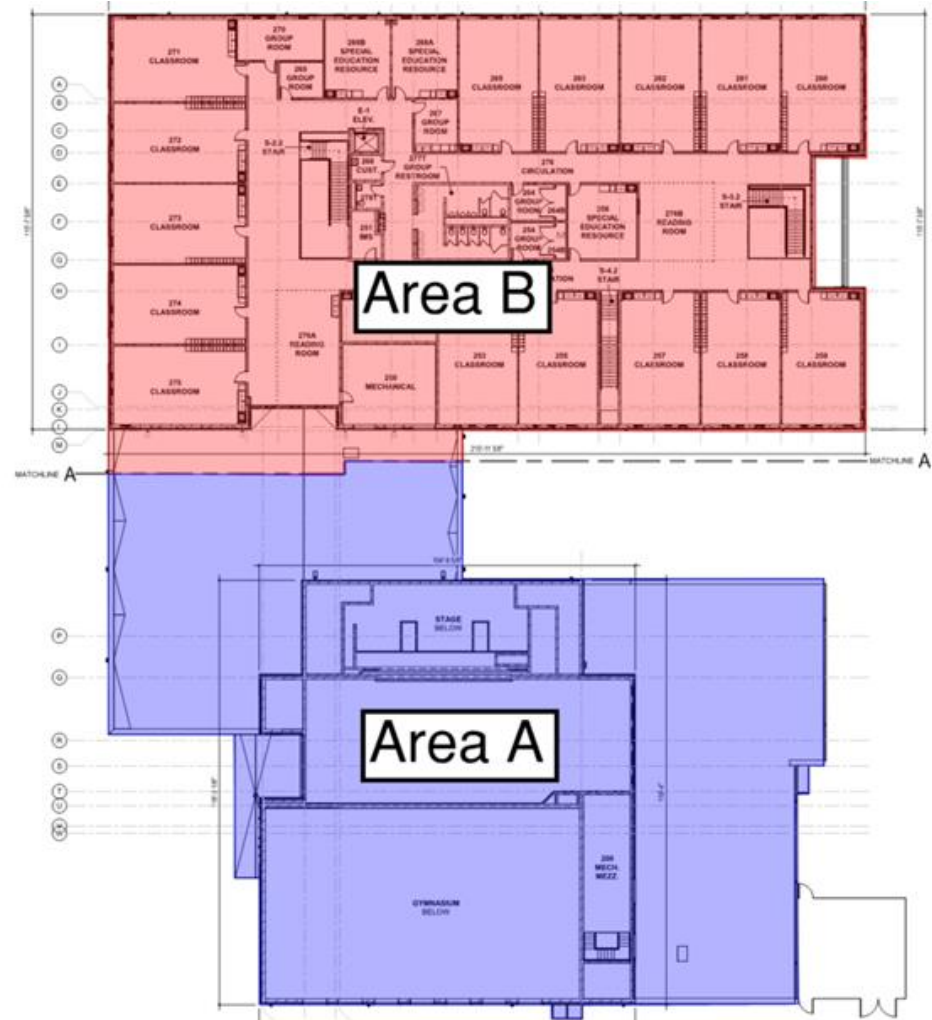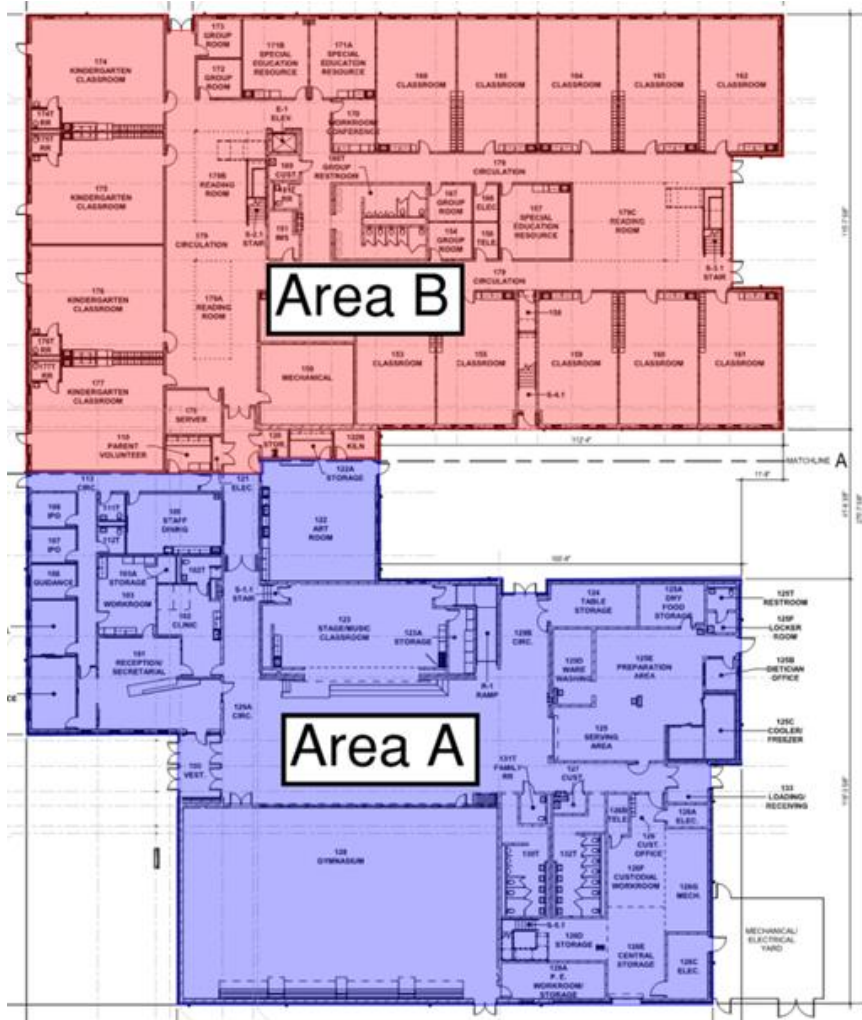

Junior High School Floor Plans

