

Harrison Elem. Weekly Blitz: December 4th, 2020



Harrison Elementary: In Area A, the administration wing ceiling grid and the gym basketball hoops are installed. Classroom cabinets and bathroom fixtures have been installed throughout the building. Window installation continues in Area B and metal gutter work continues along the roof . The roof for the main entrance canopy is nearly complete.



Crosby Elem. Weekly Blitz: December 4th, 2020



Crosby Elementary: Ceiling grid, classroom cabinets, and window installation continues throughout Area B. In Area A, the administration wing has been painted and the ceiling grid is being installed. The soffits and subsequent painting is complete in the gym. The sidewalks have been poured around the new bus lot.



Miami Whitewater Weekly Blitz: December 4th, 2020



Miami Whitewater Elementary: Drywall finishing in the administration wing has been completed and the walls are being primed and painted. In Area B, classroom cabinets are being installed on the 1st floor while ceiling grid installation is complete on the 2nd floor. Brick continues along the Area B walls while the South entrance canopy steel has been erected. Overhead MEP rough-in continues.




Junior High Weekly Blitz: December 4th, 2020



Harrison Junior High: Roof steel is being erected above the administration wing while roof detailing is complete over the academic wing. Brick will be finished in the courtyard this week and transition over to the exterior West wall of Area B. Block walls are being painted and drywall is being hung and finished on the 2nd floor of Area A. In-wall and above ceiling MEP rough-in continues in all Areas.



Elementary School Floor Plans

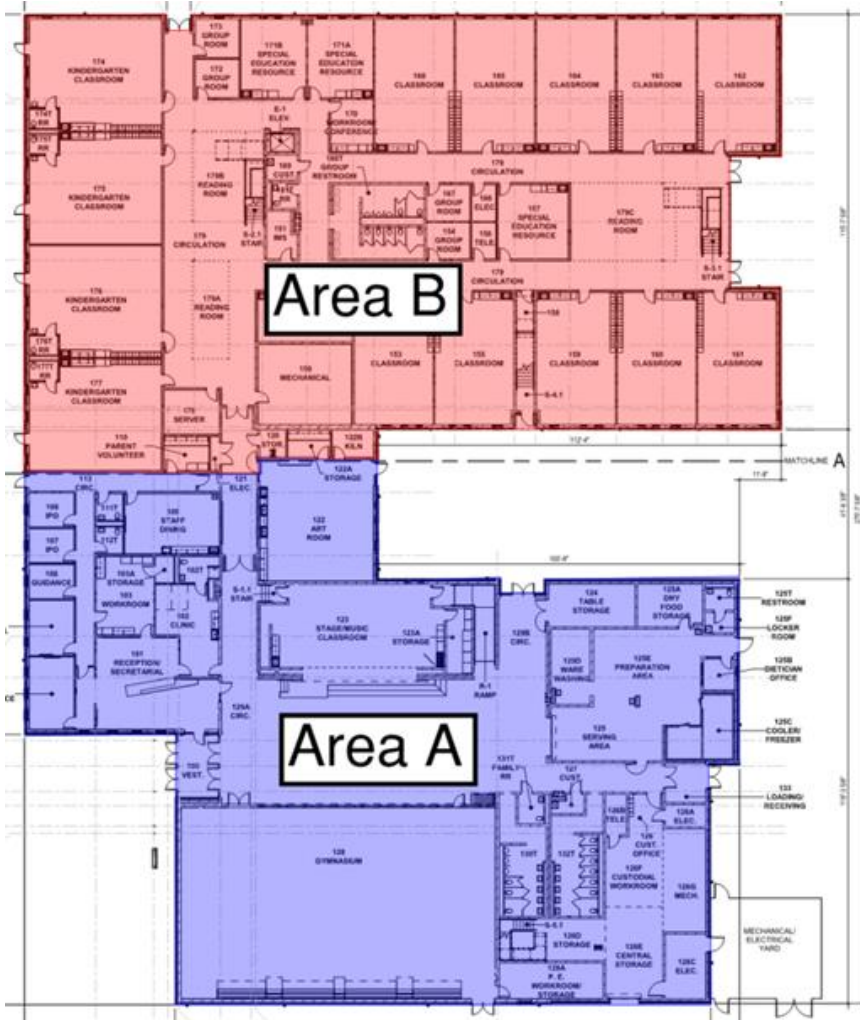

Junior High School Floor Plans

