

# Harrison Elem. Weekly Blitz: December 11<sup>th</sup>, 2020



**Harrison Elementary:** In Area A, cabinets are being installed in the administration wing and the gym wall graphics have been stenciled and painted. In the academic wing, the ceiling pads are being dropped in place on the 2<sup>nd</sup> floor and flooring is scheduled to begin next week. Window installation continues in Area B and metal gutter work continues along the roof line.





# Crosby Elem. Weekly Blitz: December 11<sup>th</sup>, 2020



**Crosby Elementary:** Classroom cabinet and window installation continues throughout Area B. In Area A, the administration wing ceiling grid is being installed while the stage gets painted. The brick on the exterior of Area A has been washed and cleaned. Basketball hoops are going to be installed in the gym next week.





# Miami Whitewater Weekly Blitz: December 11<sup>th</sup>, 2020



**Miami Whitewater Elementary:** Painting continues in the administration wing with ceiling grid installation following closely behind. The stage soffits are being framed and finished as the gym block fill continues. Ceiling grid installation is complete on the 2<sup>nd</sup> floor of Area B. Brick continues along the Area B walls.







# Junior High Weekly Blitz: December 11<sup>th</sup>, 2020



**Harrison Junior High:** Roof steel is complete above the administration wing while roofing continues above Areas B & C. Brick continues in the courtyard and on the West wall of Areas A & B. Drywall is being hung on the 1<sup>st</sup> floor of Area A while drywall finishing is complete on the 2<sup>nd</sup> floor. In-wall and above ceiling MEP rough-in continues in all Areas.



# Elementary School Floor Plans

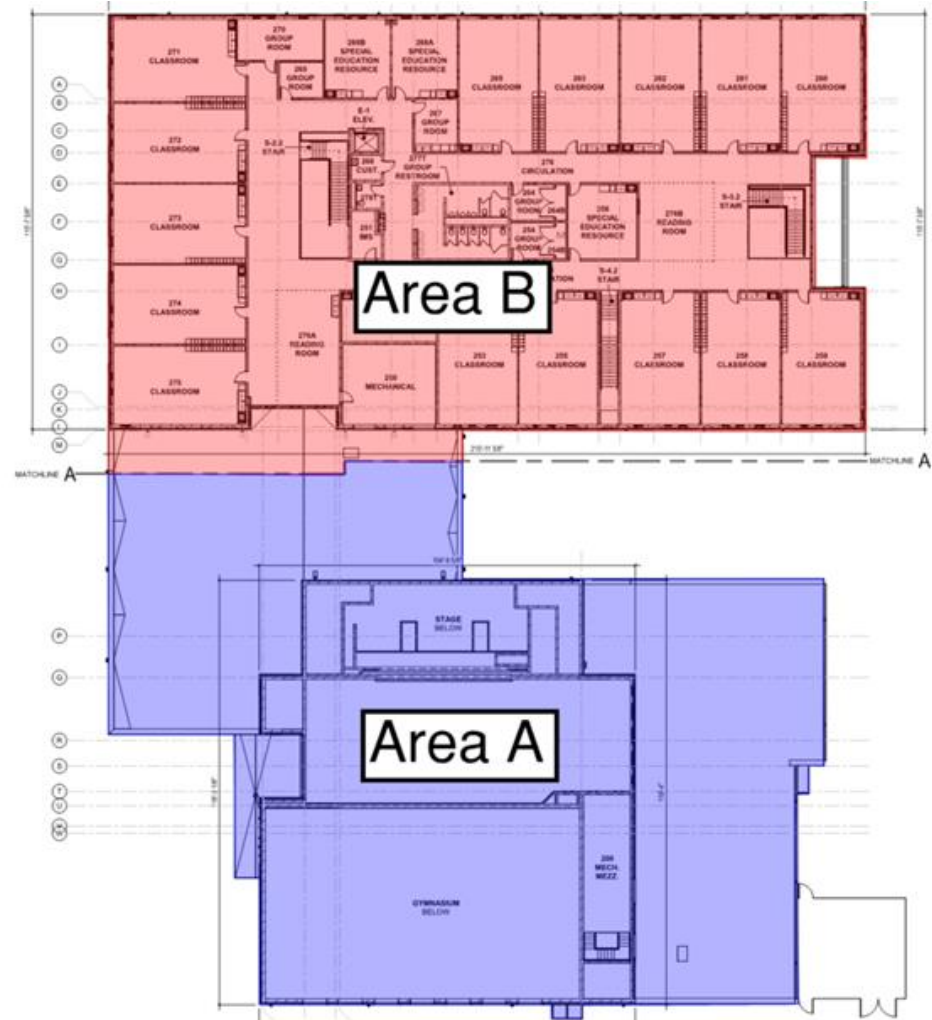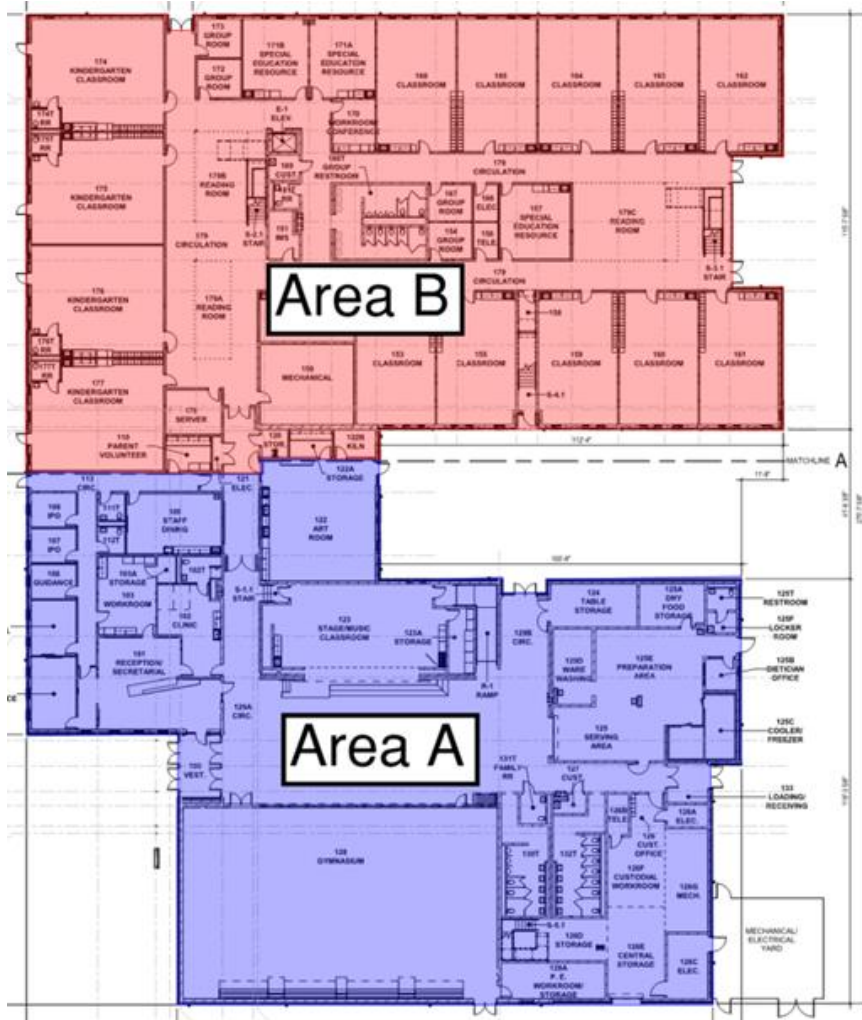



# Junior High School Floor Plans

