

Harrison Elem. Weekly Blitz: January 8th, 2021




Harrison Elementary: Final painting and soft flooring installation continues throughout the Academic and Administration wing. Ceiling grid has been installed in Area A. Miscellaneous items are being installed throughout the building such as toilets, sinks, wall protection, doors, tech devices and the coiling loading dock door. The gutters are complete along the roof of the school and the exterior site lighting has been installed.



Crosby Elem. Weekly Blitz: January 8th, 2021



Crosby Elementary: In Area A, painting and light installation continues in the gym, stage, student dining, and kitchen. Interior window trim pieces are being installed in Area B and gutter installation has begun. The exterior main entrance and bus lot entrance canopies are being framed in preparation of roofing. Exterior lighting and storm drainage underground work continues.

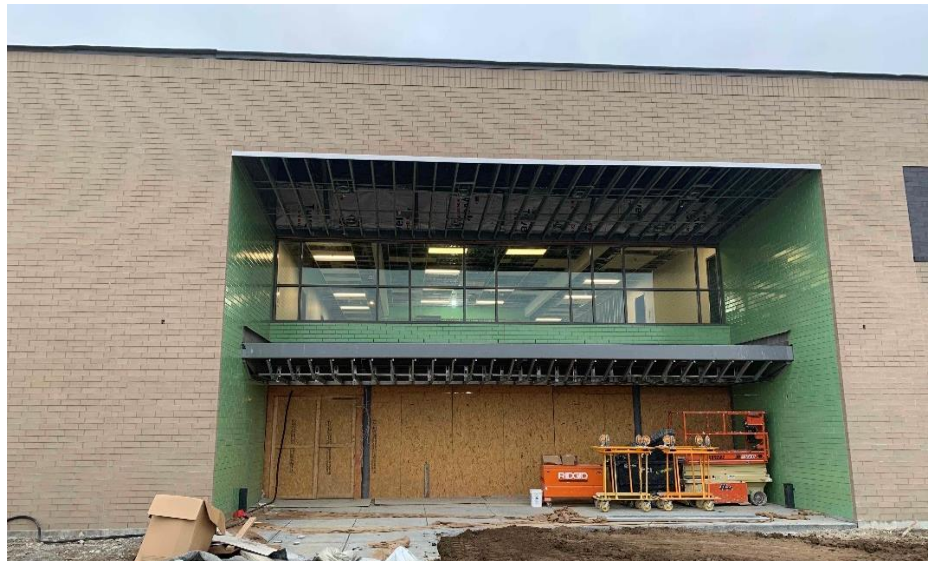

Miami Whitewater Weekly Blitz: January 8th, 2021



Miami Whitewater Elementary: Painting continues in the gym and student dining while ceiling grid is installed at the stage. Handrail and cabinet installation is nearly complete in Area B and continues in Area A. The resinous flooring in the Area B restrooms is slated to at the end of the week. On the exterior of the building, brick and metal gutter work continues along the Area B walls.





Junior High Weekly Blitz: January 8th, 2021



Harrison Junior High: Roof installation continues above the admin area while brick continues along the North wall of Area A. Drywall is being hung on the 2nd floor of Area B and finished on the 3rd floor of Area A. Painting and ceiling grid installation continues on the 1st and 2nd floors of Area A. Window installation is complete in the courtyard.



Elementary School Floor Plans

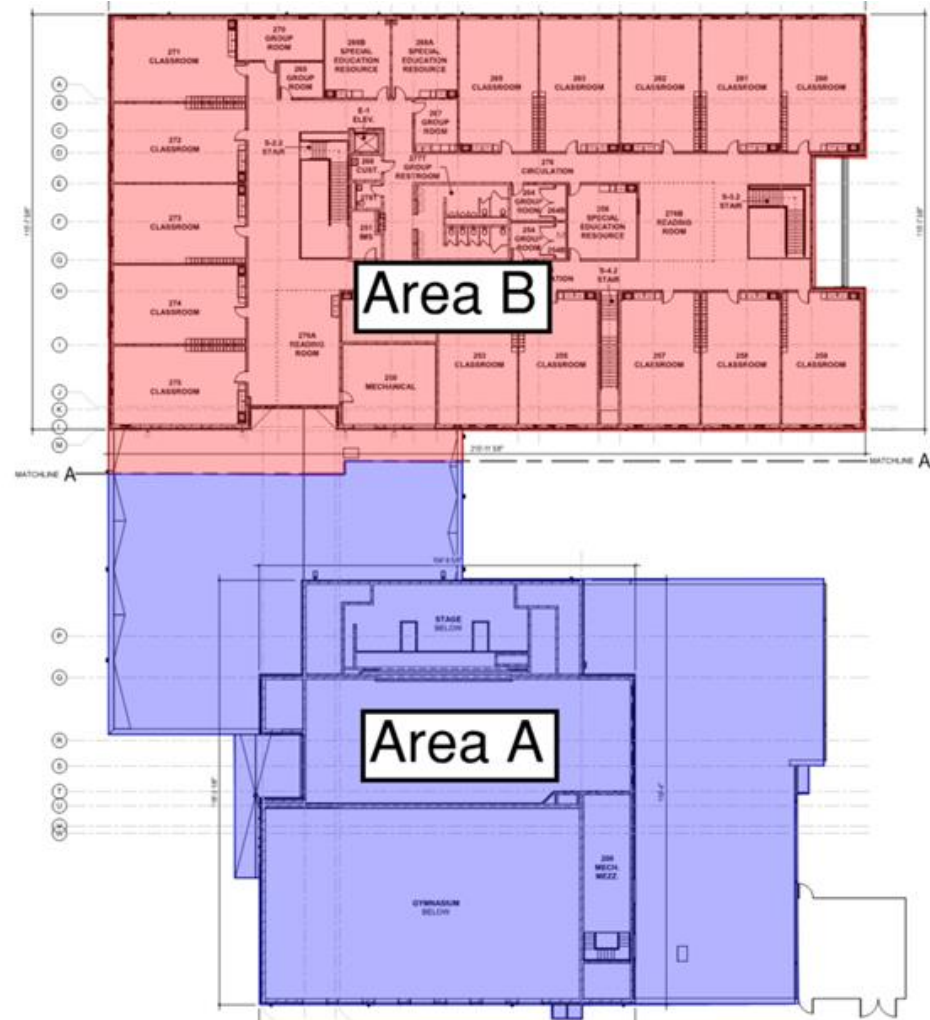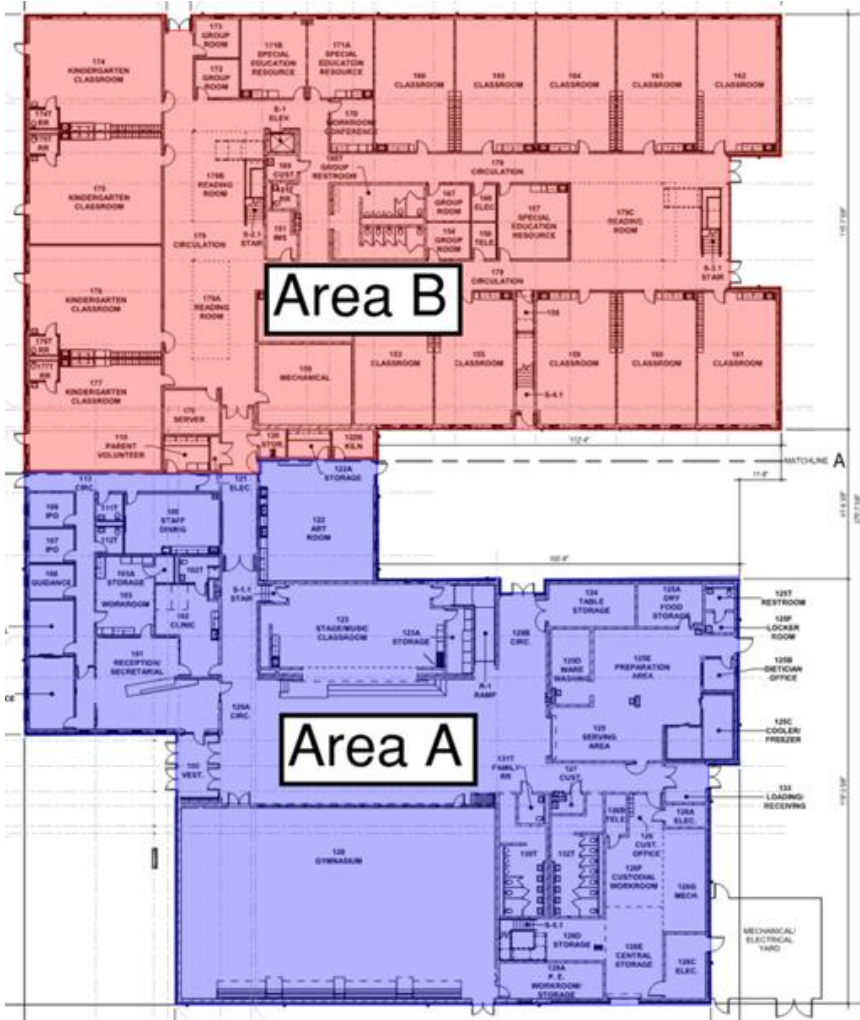

Junior High School Floor Plans

