


Harrison Elem. Weekly Blitz: February 12th, 2021



Harrison Elementary: Flooring has begun on the Stage. Metal wall panels are being installed along the exterior of Area B. Miscellaneous finish items are being installed throughout the building such as projectors, technology devices, doors, marker boards, and kitchen equipment. Furniture installation continues.

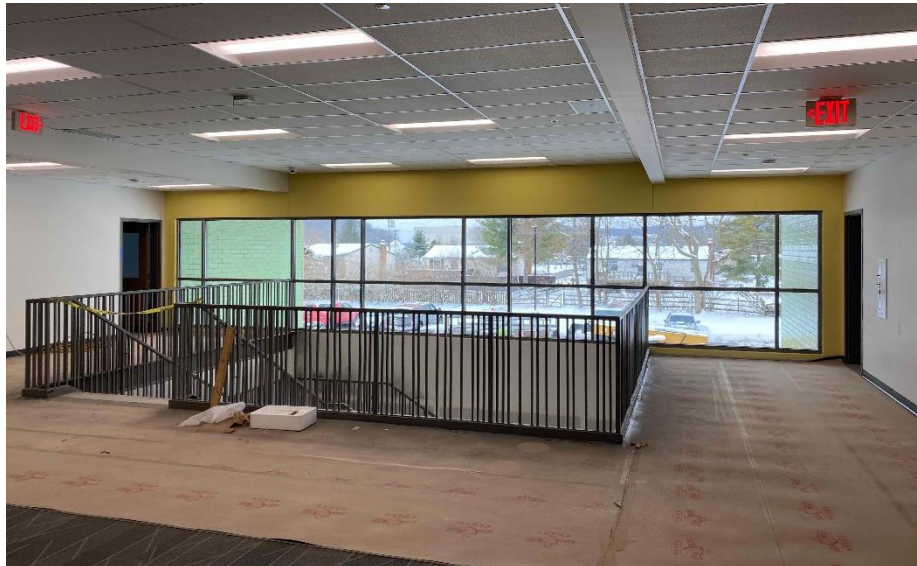

Crosby Elem. Weekly Blitz: February 12th, 2021




Crosby Elementary: In Area A, kitchen equipment installation continues while the athletic gym flooring has begun this week. Final painting and soft flooring continues across the academic wing. Gutters and downspouts are being installed along the exterior of the building. Exterior door hardware is being installed on exterior openings and storefronts.



Miami Whitewater Weekly Blitz: February 12th, 2021



Miami Whitewater Elementary: Brick work is ongoing in Area A while window installation continues around Area B. Ceiling pads are being dropped in the Art room and Stage. Soft flooring continues in the classrooms while the expoy floor prep work is finished in the kitchen. Plumbing fixtures are being installed throughout the building.

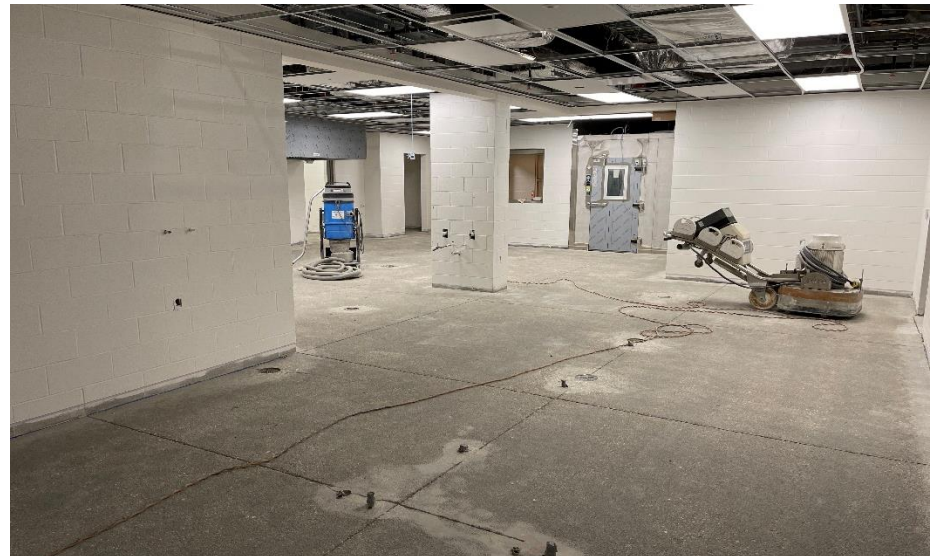



Junior High Weekly Blitz: February 12th, 2021



Harrison Junior High: Brick work is ongoing around Areas A and B with window installation following closely behind. The concrete steps have been poured in the learning stairs in the student dining area. Drywall is being hung in the Area C Life Skills room and finished throughout Area B. The interior drywall partitions are being framed up in the administration wing.



Elementary School Floor Plans

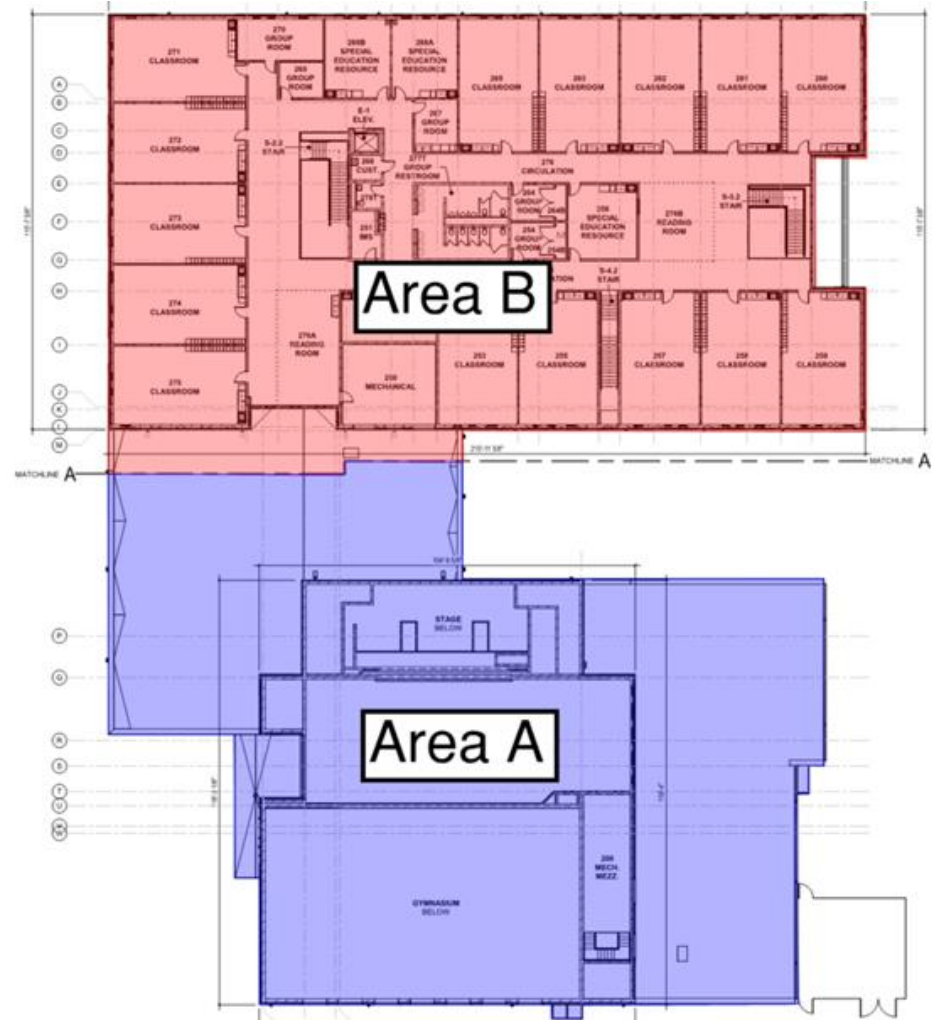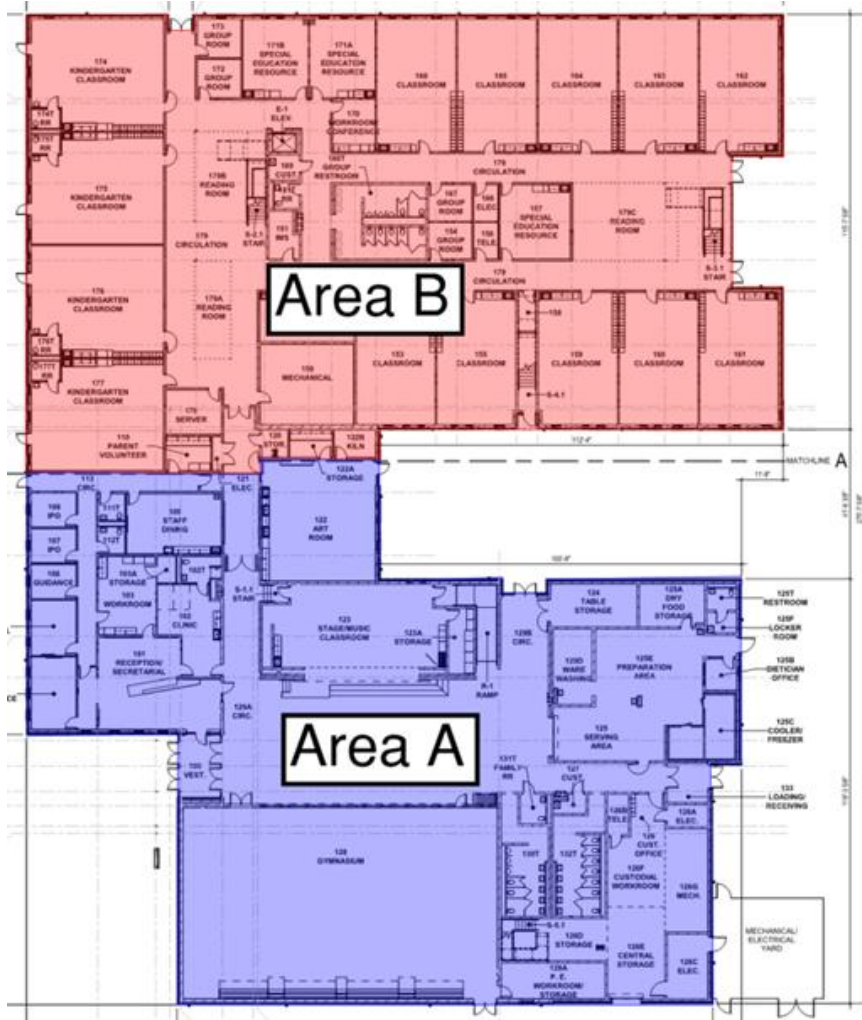

Junior High School Floor Plans

